

## January-February 2025 - Project Dashboard

### Project 19357 McNab Road and Bridge Improvements

#### Prime Consultant:

**Kimley»Horn**

#### CMAR:

**BURKHARDT  
CONSTRUCTION, INC.**

#### City of Pompano Beach

GO BOND DIRECTOR: FERNAND THONY, PE

PROJECT MANAGER: FERNAND THONY, PE

CURRENT PHASE: CONSTRUCTION


DESIGN TEAM: KIMLEY HORN

CONSTRUCTION TEAM: HA CONTRACTING CORP.

GO BOND BUDGET: **\$16,500,000.00**

APPROVED CONTRACT **\$22,936,498.77**

#### PROJECT PHOTOS (EXISTING & PROPOSED CONCEPT)

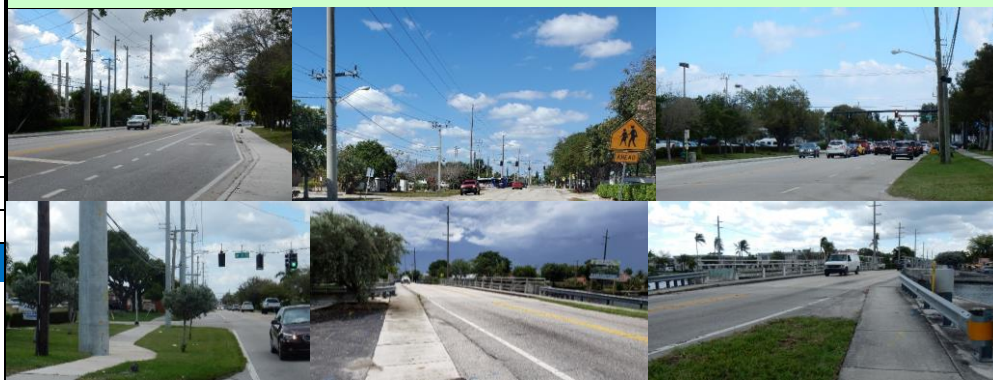

#### PROJECT OBJECTIVES

The project main objectives include replacing the existing functionally obsolete bridge over C-14 on McNab Road and beautifying McNab Road corridor between Federal Highway and South Cypress Creek Road. The project will modernize the area by laying new paving, related drainage improvements, ADA sidewalks, street and pedestrian lighting, landscaping, bus shelters/benches and street furnishings.


#### PROJECT UPDATES

The McNab Road and Bridge improvements project has progressed steadily toward the construction phase. Staff worked with Procurement & Contracts Department to issue a solicitation RFQ E-11-24 in June 2024. Final responses and proposals were reviewed and a general contractor was selected for award. Negotiations have been held and BAFO (best and final offer) received in November 2024. An agenda item is being finalized with the City Attorney's office which is anticipated to be ready for submittal to the City Commission's consideration in March 2025. Upon approval and award of the City Commission, a building permit will be secured by the new contractor and the project and construction activities are expected to begin on or around May 2025.

#### CONSTRUCTION:

Streetscape Work including, flatwork, stormwater, utilities ,etc... Start: May/June 2025 End: November 2026

Bridge Work including demolition, pile and deck construction... Start: May - 2026 End: September 2026

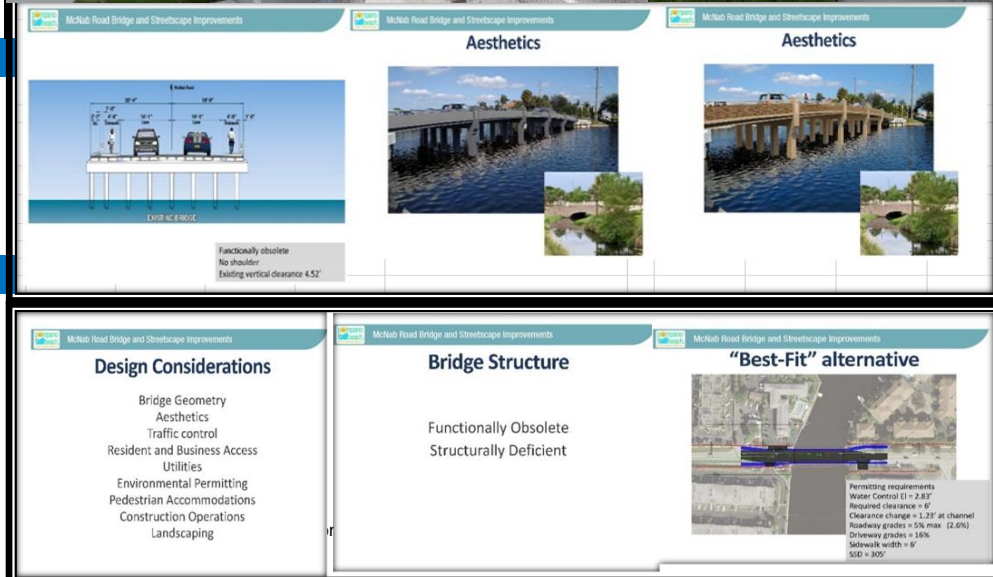

#### PROJECT SITE LOCATION

